Project Meridian

Skyway 4.0 Platform Migration - Monthly Status Report

Reporting period: 1-31 July 2026 | PMO: Dana Okafor


Executive Status: On Track

- Overall status is GREEN; schedule variance is +4 days
- Fleet-controller cutover completed for 31 of 46 pilot sites
- Data migration dry run finished with 0 blocking defects
  - Two medium defects in telemetry backfill, fixes in review
- Risk: certification lab availability in September (mitigation booked with second lab in Denver)
- Budget consumed: $3.42M of $5.10M approved (67%)

Key Metrics vs. Plan

Metric	Plan (Jul)	Actual (Jul)	Variance
Sites cut over	28	31	+3
Open defects (sev 1-2)	0	0	0
Open defects (sev 3)	12	9	-3
Fleet uptime during cutover	99.50%	99.74%	+0.24 pt
Migration cost per site ($K)	74.0	69.8	-4.2
Trained site operators	180	196	+16

Delivery Timeline

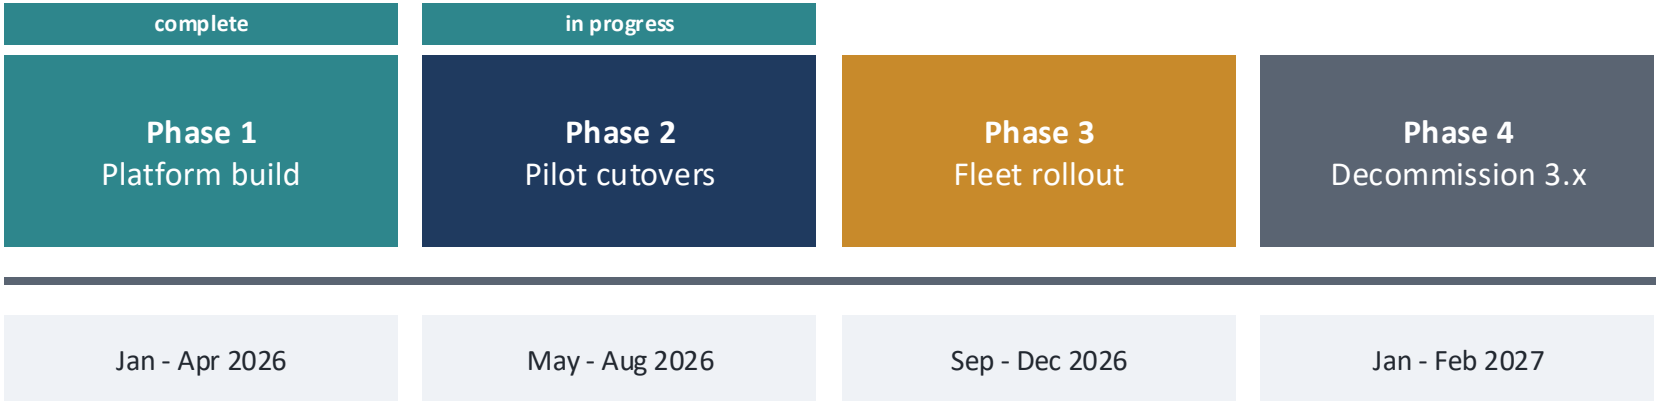



Summary and Asks

- Project remains on schedule and 4% under budget
- Pilot exit review scheduled for 21 August 2026
- Ask: approve $180K contingency for second certification lab
- Ask: confirm freeze window for the September fleet rollout
- Next report: 29 August 2026
